

25X1A


To:

Oct. 13, 1959

From:

Subject: PROJECT MEMO #9 - PRODUCTION SCHEDULE, A-12

Because of engine changes and configuration problems, the first flight will be 20 months from go-ahead. All 12 airplanes will, however, be done in 36 months.

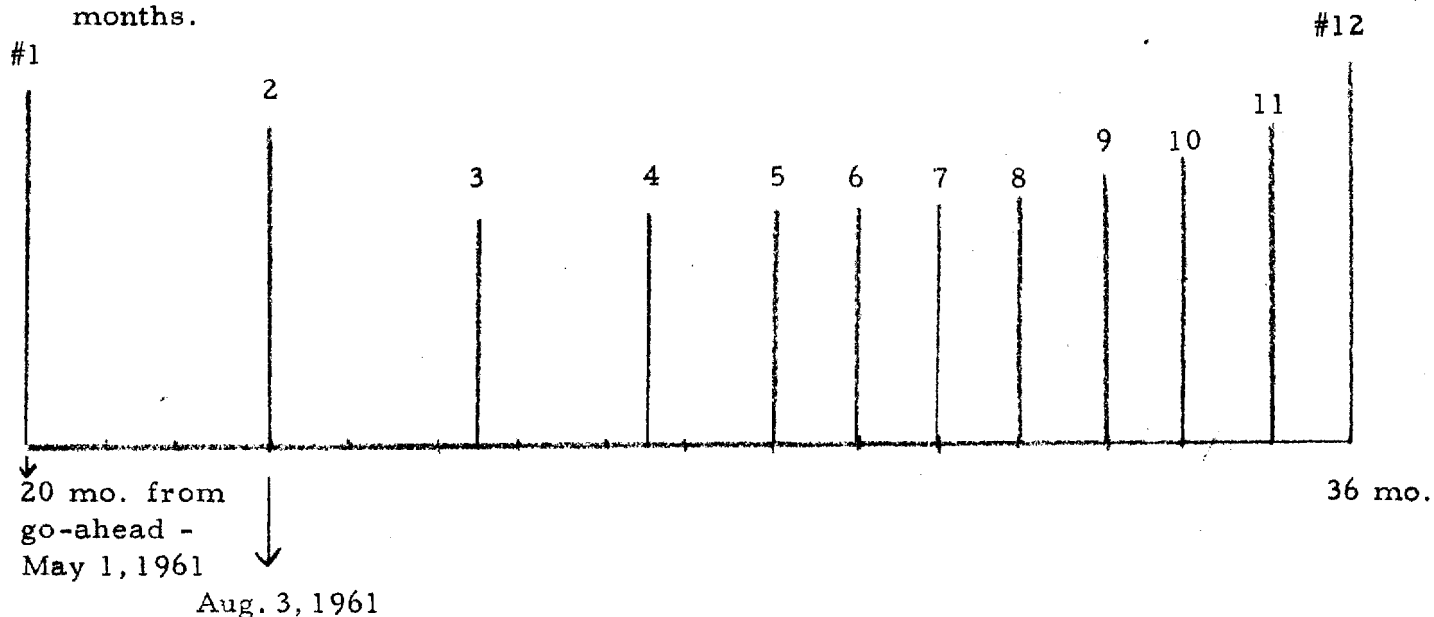

25X1A

Delivery to Customer

Have to deliver aircraft to ranch approximately one month prior to above dates to provide time for re-assembly and production test.

#1	May 1, 1961	#5	Feb. 7, 1962	#9	June 13, 1962
#2	Aug. 3, 1961	#6	Mar. 7, 1962	#10	July 11, 1962
#3	Oct. 18, 1961	#7	Apr. 11, 1962	#11	Aug. 10, 1962
#4	Dec. 20, 1961	#8	May 11, 1962	#12	Sept. 5, 1962


*Clarence L. Johnson*  
Clarence L. Johnson

Vice President

Advanced Development Projects

# PROTOTYPE A-12 SCHEDULE

Approved For Release 2000/08/26 : CIA-RDP62B00844R000200120011-8

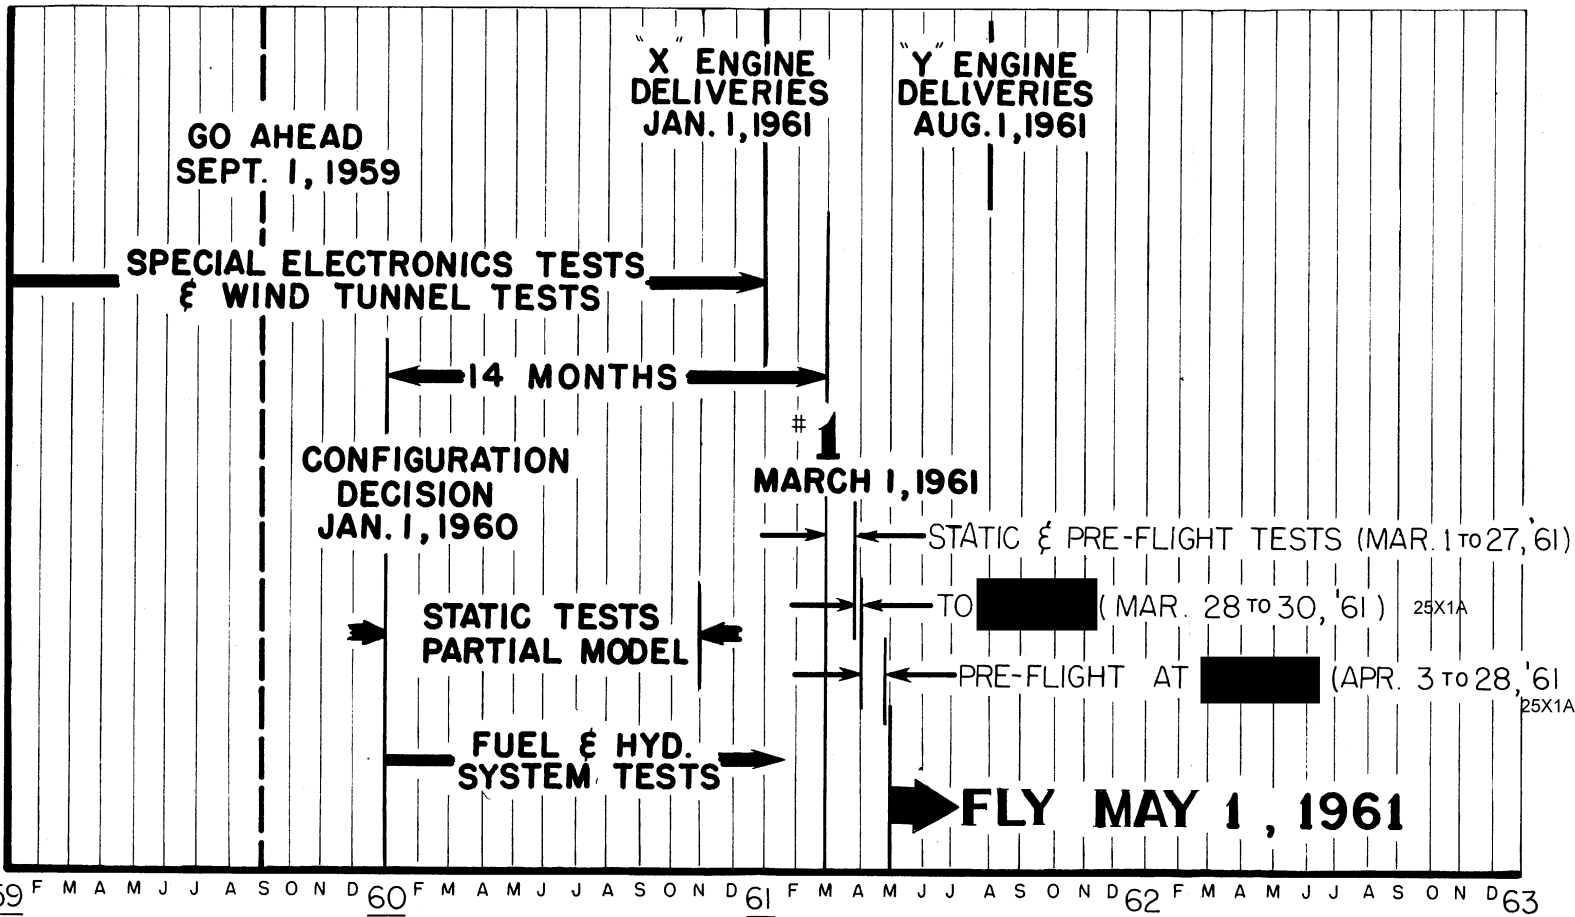

*Clarence L. Johnson*  
 Clarence L. Johnson  
 Vice President  
 Advanced Development Projects
